Oklahoma Corporation Commission
Oil & Gas Conservation Division
Post Office Box 52000
Oklahoma City, Oklahoma 73152-2000
Rule 165: 10-3-25

Form 1002A

API No.: 35063245870000

Completion Report

Spud Date: January 11, 2016

OTC Prod. Unit No.: 063217574000

Drilling Finished Date: April 19, 2016

1st Prod Date: June 21, 2016

Completion Date: May 27, 2016

Drill Type: **HORIZONTAL HOLE**

Well Name: LYNN 4-14H

Purchaser/Measurer: UNIMARK

Location: HUGHES 23 7N 11E
NE SE NE NW
977 FNL 2395 FWL of 1/4 SEC
Latitude: 35.0696944 Longitude: 35.0696944
Derrick Elevation: 836 Ground Elevation: 813

First Sales Date: 6/21/2016

Operator: PETROQUEST ENERGY LLC 21466

1717 S BOULDER AVE STE 201
TULSA, OK 74119-4842

Completion Type	
X	Single Zone
	Multiple Zone
	Commingled

Location Exception
Order No
647930
652609

Increased Density
Order No
648686

Casing and Cement

Type	Size	Weight	Grade	Feet	PSI	SAX	Top of CMT
SURFACE	13.375	48	J-55	411		195	SURFACE
INTERMEDIATE	9.625	36	J-55	2970		325	414
PRODUCTION	5.5	20	P-110	10825		1195	2751

Liner

Type	Size	Weight	Grade	Length	PSI	SAX	Top Depth	Bottom Depth
There are no Liner records to display.								

Total Depth: 10839

Packer	
Depth	Brand & Type
10738	TOE SLEEVE

Plug	
Depth	Plug Type
There are no Plug records to display.	

Initial Test Data

Test Date	Formation	Oil BBL/Day	Oil-Gravity (API)	Gas MCF/Day	Gas-Oil Ratio Cu FT/BBL	Water BBL/Day	Pumpin or Flowing	Initial Shut-In Pressure	Choke Size	Flow Tubing Pressure
Jun 29, 2016	WOODFORD			1214		1739	FLOWING		OPEN	200

Completion and Test Data by Producing Formation

Formation Name: WOODFORD Code: 319WDFD Class: GAS

Spacing Orders

Order No	Unit Size
540286	640

Perforated Intervals

From	To
5364	7052
7955	10643

Acid Volumes

12,310 GALS

Fracture Treatments

6,372,405 GALS SLICKWATER, 4,131,600 SAND

Formation	Top
WAPANUKA	3843
CROMWELL	4179
CANEY	4752
MAYES	4999
WOODFORD	5210

Were open hole logs run? No
Date last log run:

Were unusual drilling circumstances encountered? No
Explanation:

Other Remarks

IRREGULAR SECTION.

Lateral Holes

Sec: 14 TWP: 7N RGE: 11E County: HUGHES

NW NW NE NW

1 FNL 1634 FWL of 1/4 SEC

Depth of Deviation: 4326 Radius of Turn: 636 Direction: 355 Total Length: 4376

Measured Total Depth: 10839 True Vertical Depth: 4975 End Pt. Location From Release, Unit or Property Line: 1

FOR COMMISSION USE ONLY

1133830

Status: Accepted

PetroQuest Well Location Plat

S.H.L. Sec. 23-7N-11E I.M.
B.H.L. Sec. 14-7N-11E I.M.

Operator : PETROQUEST ENERGY, LLC
Lease Name and No : LYNN 4-14H
Footage : 977' FNL - 2395' FWL GR. ELEVATION 814' Good Site? YES
Section : 23 Township : 7N Range : 11E I M
County : Hughes State of Oklahoma
Alternate Loc : N/A
Terrain at Loc : Location fell in level pasture, ±195' North of an E-W pipeline, ±250' West of a N-S fence

Accessibility : From the North
Directions : From the town of Lamar, OK, go 1 5 miles South on "NS 387 Rd." to the Northwest Corner of Section 23-7N-11E.

1"=1320'

GPS DATUM
NAD - 27
OK SOUTH ZONE

Surface Hole Loc :
Lat: 35°04'10.90"N
Lon: 96°06'56.64"W
X: 2563825
Y: 637156

Point of Entry :
Lat: 35°04'20.57"N
Lon. 96°07'05.83"W
X: 2563044
Y: 638119

Bottom Hole Loc :
Lat: 35°05'12.88"N
Lon. 96°07'05.93"W
X: 2562937
Y: 643406

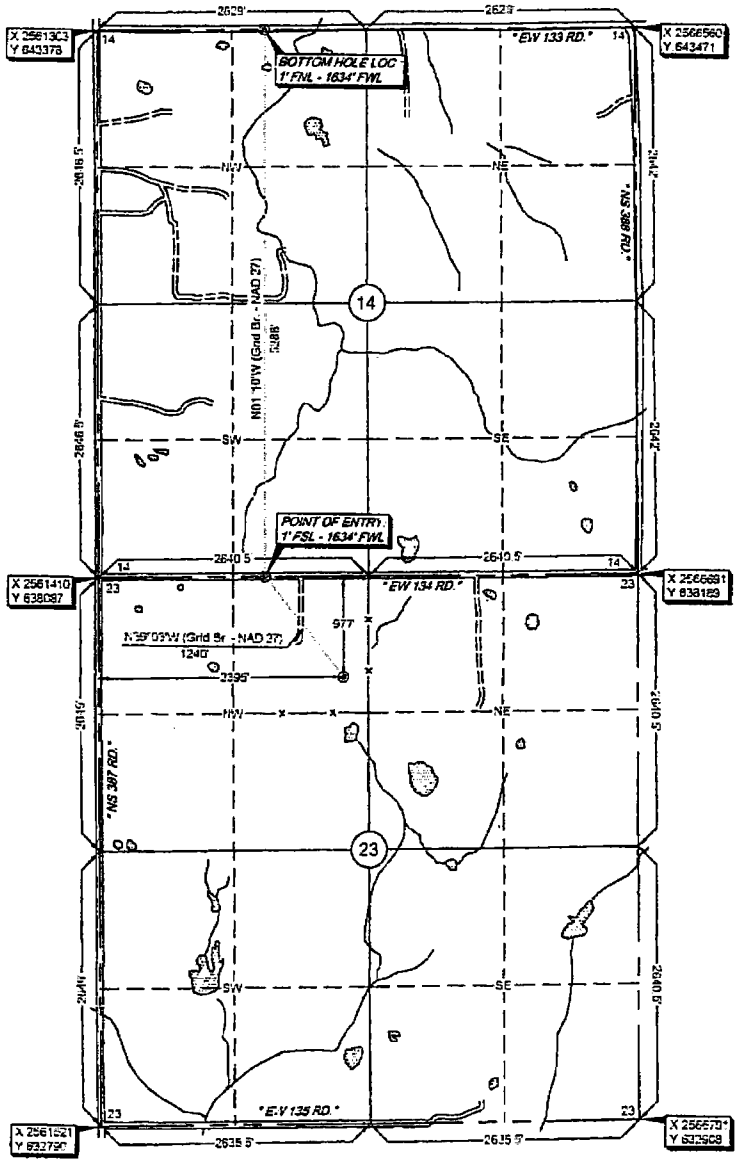

Quarter Section distances may be assumed from a Government Survey Plat or assumed at a proportionate distance from opposing section corners, or occupation thereof, and may not have been measured on the ground, and further, does not represent a true boundary survey

Please note that this location was staked on the ground under the supervision of a Licensed Professional Land Surveyor, but the accuracy of this survey is not guaranteed Please contact Arkoma Surveying and Mapping promptly if any inconsistency is determined GPS data is observed from RTK - GPS

NOTE: X and Y data shown hereon for Section Corners may NOT have been surveyed on the ground, and further, does NOT represent a true Boundary Survey.

survey and plat by
Arkoma Surveying and Mapping, PLLC
P.O. Box 238 Wilburton, OK 74578
Ph. 918-465-5711 Fax 918-465-5030
Certificate of Authorization No. 5348
Expires June 30, 2016

Invoice #5866-A-C
Date Staked : 12/09/15 By : C K
Date Drawn : 12/10/15 By : J H.

Certification
This is to certify that this Well Location Plat represents the results of a survey made on the ground performed under the supervision of the undersigned

LANCE G MATHIS 12/10/15
LANCE G MATHIS OK LPLS 1664

LICENSED PROFESSIONAL LAND SURVEYOR
LANCE G. MATHIS
1664
OKLAHOMA

6/21/16

Oklahoma Corporation Commission
Oil & Gas Conservation Division
Post Office Box 52000
Oklahoma City, Oklahoma 73152-2000
Rule 165: 10-3-25

Form 1002A

1016EZ

API No.: 35063245870000

OTC Prod. Unit No.: 063217574000

A: 217574 I

Completion Report

Spud Date: January 11, 2016

Drilling Finished Date: April 19, 2016

1st Prod Date: June 21, 2016

Completion Date: May 27, 2016

Drill Type: **HORIZONTAL HOLE**

BHL: 14-07N-11E

Well Name: LYNN 4-14H

Purchaser/Measurer: UNIMARK

First Sales Date: 6/21/2016

Location: HUGHES 23 7N 11E SL
NE SE NE NW
977 FNL 2395 FWL of 1/4 SEC
Latitude: 35.0696944 Longitude: 35.0696944
Derrick Elevation: 836 Ground Elevation: 813

Operator: PETROQUEST ENERGY LLC 21466

1717 S BOULDER AVE STE 201
TULSA, OK 74119-4842

Completion Type	
X	Single Zone
	Multiple Zone
	Commingled

Location Exception
Order No
647930
652609

Increased Density
Order No
648686

sep. allow: 648688

Casing and Cement

Type	Size	Weight	Grade	Feet	PSI	SAX	Top of CMT
SURFACE	13.375	48	J-55	411		195	SURFACE
INTERMEDIATE	9.625	36	J-55	2970		325	414
PRODUCTION	5.5	20	P-110	10825		1195	2751

Liner

Type	Size	Weight	Grade	Length	PSI	SAX	Top Depth	Bottom Depth
There are no Liner records to display.								

Total Depth: 10839

Packer	
Depth	Brand & Type
10738	TOE SLEEVE

Plug	
Depth	Plug Type
There are no Plug records to display.	

6/29/16 319WDFD 1 XMT-shale

EZ

OK
